



UPDATE ON THE IMPLEMENTATION OF THE TPB'S TIGER GRANT

Priority Bus Transit in the National Capital Region

Eric Randall
TPB Transportation Engineer

Transportation Planning Board
May 18, 2016



Overview of the TIGER Grant

- The TPB's Transportation Investments Generating Economic Recovery (TIGER) Grant Agreement with USDOT was signed on December 14, 2010.
- \$58.8 million in capital funding (100% Federal) for priority bus transit improvements
- Fifteen component projects with five implementing organizations: City of Alexandria, DDOT, MDOT, PRTC, and WMATA.



TIGER Projects Complete

- PRTC Buses
- Potomac Yard Transitway (Alexandria)
- Real-Time Passenger Information Signs (DDOT, MDOT, WMATA, Alexandria)
- Downtown Signal Optimization (DDOT)





Potomac and Rappahannock Transportation Commission (PRTC)

- 13 replacement buses delivered in 2012.



City of Alexandria Potomac Yard Transitway

- Dedicated travel lanes for bus in median of US 1, opened for service August 2014.






Real Time Passenger Information – DDOT, MDOT, WMATA, Alexandria

167 RTPI signs installed (Nov 2014–April 2015)

- 16th Street (31)
- Georgia Avenue (23)
- H St / Benning Rd (28)
- Wisconsin Avenue (38)
- Addison Road (5)
- University Blvd (10)
- Veirs Mill Road (8)
- Pentagon and Franconia-Springfield Stations (22)

12 RTPI signs awaiting completion of shelters



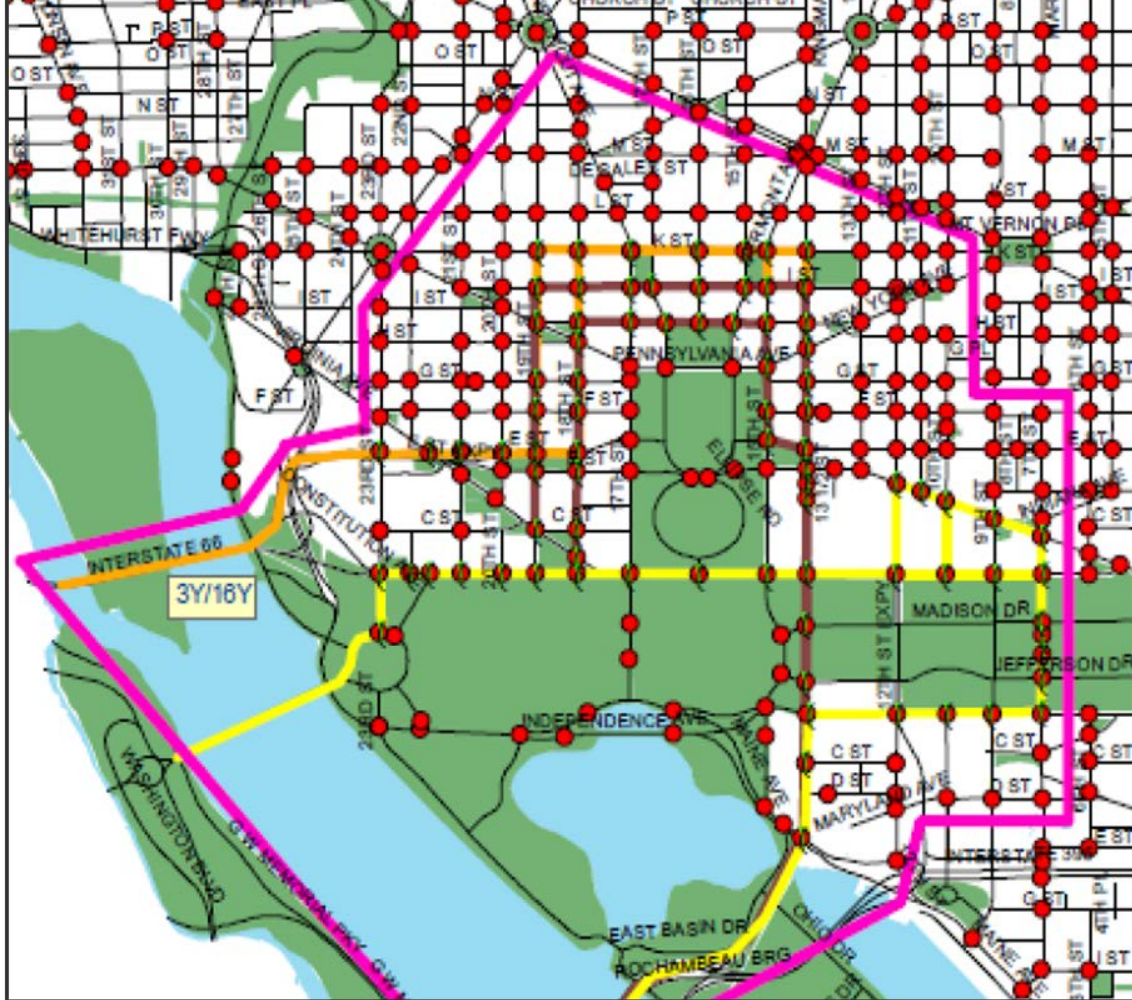

DC Traffic Signal Optimization TR Bridge and 14th Street Bridge to K Street


- 208 traffic signals optimized



TIGER Projects Nearing Completion

- Takoma/Langley Transit Center (MDOT/MTA)
 - Anticipate construction completion this month. WMATA to install additional items and open for service around August.
- Pentagon and Franconia Springfield Transit Stations (WMATA)
 - Construction largely complete at Pentagon with completion of security technology projects anticipated this month.
 - Franconia Springfield construction in progress, to complete by end of June
- Georgia Avenue Bus-Only Lane (DDOT)
 - Open for service, final details to be installed end of this month.
- PRTC Computer Assisted Dispatch / Automated Vehicle Location (CAD/AVL) System
 - All technology deployed, with final acceptance in progress



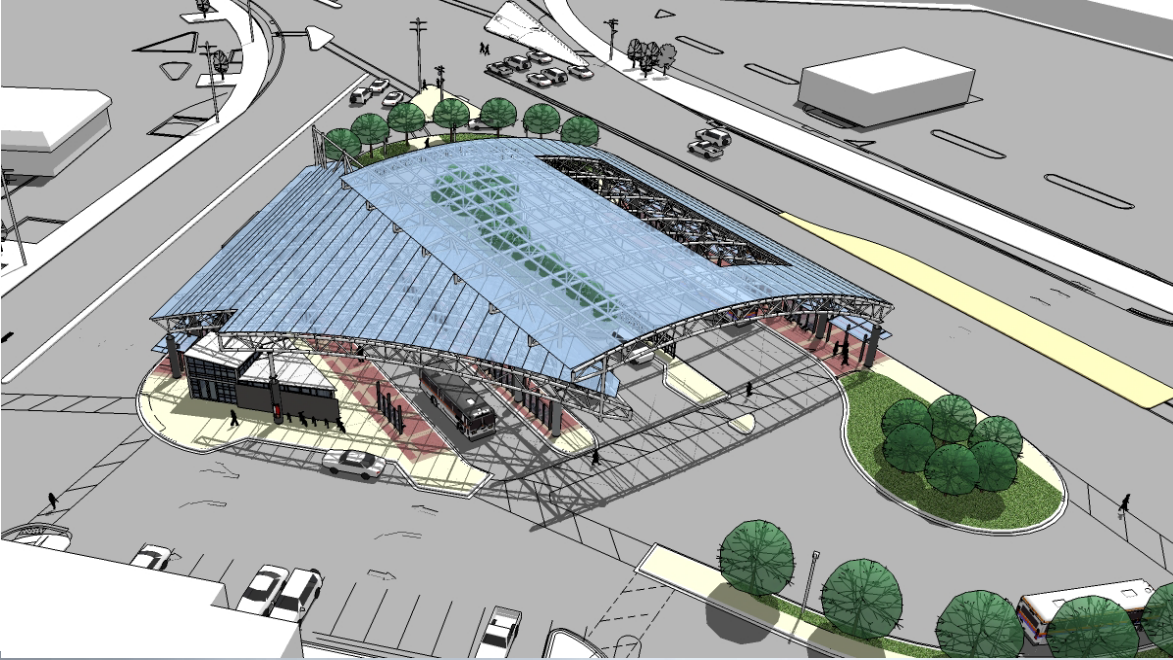

Takoma - Langley Crossroads Transit Center (MDOT/MTA)

- Largely complete
- MTA anticipates May 23 date for completion
- WMATA will takeover in June and install final furnishings.





Pentagon and Franconia-Springfield Transit Stations (WMATA)

- Final technology systems installation at Pentagon
- Bus Canopy installation at Franconia Springfield
- Both to complete in June



Georgia Avenue Bus Lane (DDOT)

- Opened for operation on April 11, 2016.
- Final red high-friction paving treatment to be installed end of May.
- Minor added work including bus stop relocations and sidewalk flexible porous pavement installation.



TIGER Project In Progress

- Transit Signal Priority (TSP)
(Alexandria, DDOT, WMATA)
 - TSP installation complete on VA 7
(Leesburg Pike). Operational testing
continues.
 - Almost 200 signal locations in the District
installed with technology. Onboard bus
equipment is being installed by WMATA
on 116 Metrobuses. Prototype testing is
complete.
 - TSP installed at nine locations along the
Van Dorn-Pentagon corridor in February.
WMATA is working to get onboard
equipment installed on buses. The City
and WMATA are coordinating on central
system access and management.



- The grant-funded part of the project
should be completed in July.
- However operational testing will
continue and implementation will
become part of ongoing operations.



TIGER Grant Progress and Funds Expiration

- Progress to Date / Remaining

	<u>To Date:</u>	<u>Remaining:</u>
Period of Performance:	Five years, four months (93%)	5 months to go (7%)
Actual/Anticipated Expenditures:	\$44.6 million (76%)	\$14.2 million (24%)

- Grant – Work must be completed by the end of June 2016 to ensure timely invoicing before funds expire in September 2016.



Eric Randall

TPB Transportation Engineer

(202) 962-3254

erandall@mwkog.org

mwkog.org/TPB

Metropolitan Washington Council of Governments

777 North Capitol Street NE, Suite 300

Washington, DC 20002



National Capital Region
Transportation Planning Board
